

Welcome to Wheaton Revitalization News!

Wheaton Revitalization News is an email distribution list that will provide frequent updates to the surrounding community on the Wheaton Revitalization project. The purpose of this distribution list is to provide you with project updates and construction activities. For additional information on the Wheaton Revitalization Project please visit <http://www.wheatonproject.com>

Look Ahead - Week of June 24 to June 30, 2018

Headliner

The second (2nd) concrete pour for the bottommost garage floor (Level P4) was completed on June 20, 2018.

Executive Summary

The project continues to track for an April 2020 substantial completion.

Level P4 and Footer Construction

The bottommost level of the garage, known as Level P4, remains under construction. Level P4 will be constructed in 10-phases (10-concrete pours). Pour two (2) was completed this week and Pour 3 is expected to take place on July 6.

Numerous quality assurance/quality control (QA/QC) inspections are conducted daily to ensure that the waterproofing and reinforcing systems have met specified QA/QC requirements. Detailed inspections of the waterproofing and reinforcing continue up to (several) hours before the pour to ensure the integrity of building systems and must be "cleared" in order for the pour to take place.


Pour #2 completed on June 20, required 650 cubic yards of concrete. Concrete is delivered in trucks carrying 10 cubic yards of concrete per truck. In all, sixty-five (65) concrete deliveries took place between 5:30 am and 4pm in orderly fashion causing little disruption to traffic flow along Grandview Avenue. Concrete deliveries were spaced such that no more than 6-trucks were at the site at any given time. The trucks queued-up behind the construction barrels along Grandview Ave.

The contractor used a large truck-mounted pump to deliver the concrete from the upper level (near the field office) of the jobsite to the point of placement in the bottom of the hole. The pump apparatus is capable of delivering 80 cubic yards per hour.

The contractor plans to make 2-pours per week wrapping up Level P4 over the next 4-weeks. Building foundation, including footers and building columns, are poured monolithically (at the same time) with garage Level P4.

The building is expected to reach the surrounding street level by Thanksgiving 2018.

Reinforcing for Pour #2

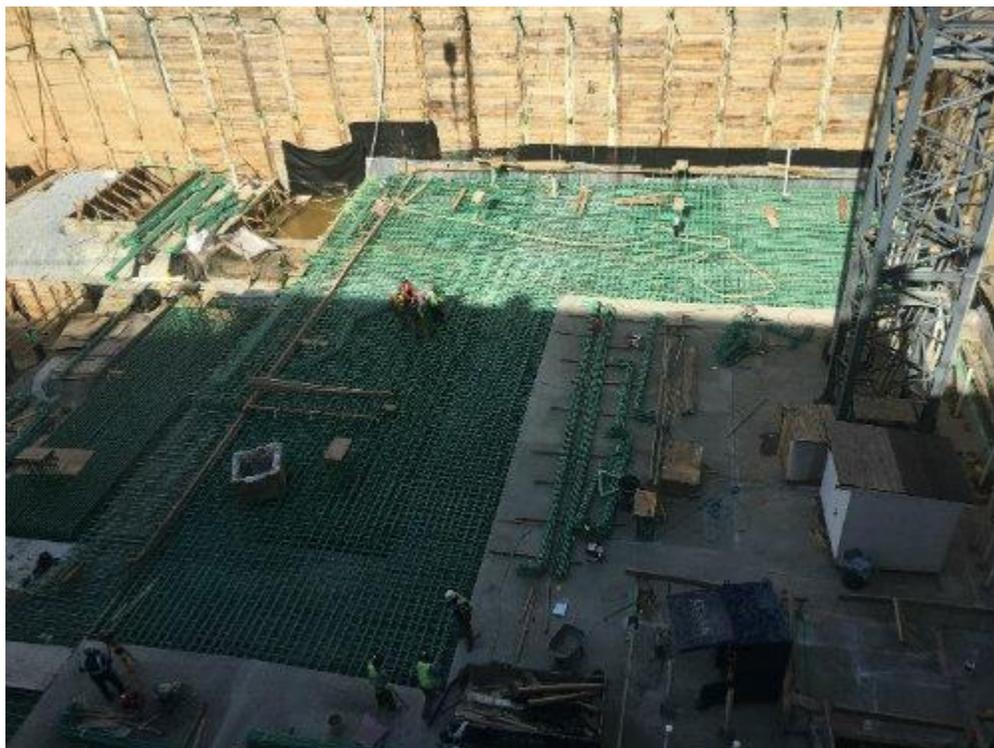

Utility Construction

Underground electric (Pepco) work will continue along Grandview Avenue and Ennalls Avenue this week. Several parking meters will be bagged on a daily basis to facilitate this work. DOT Parking Operations is the lead on bagging and un-bagging parking meters. Both DOT and the utility contractor have been careful to bag only those meters in the immediate proximity to the work and to remove bags whenever work has paused. This work is going well and expected to wrap up in the next 3 weeks.

Following installation of the underground electrical conduit along Grandview Avenue, Verizon will mobilize its crews and place underground conduit for relocation of its communication cables from overhead to underground. Soon thereafter, all overhead lines along Grandview will be removed.

Also included in the project is sanitary sewer upgrades along Reedie Drive, Grandview Ave, and Viers Mill Drive. A separate schedule will be published in an upcoming weekly report for this work.

Utility Work along Grandview Avenue



Follow Project Progress via the Project Camera

A camera has been installed to view construction on the site. ***Click here*** to access the camera.

Upcoming and Ongoing Activities

- Concrete placement for garage Level P4 over the next four (4) weeks
- Continued placement of concrete mud mat atop stone for future concrete pours
- Placement of waterproofing atop concrete mud mat
- Utility construction in Grandview Avenue and Ennals Avenue

Project Milestone Schedule

Activity	Completion Date
Demolition of RSC Bldg.	Complete ✓
Building tie-down anchors	Complete ✓
Geothermal Piping	Complete ✓
Foundation Construction	Summer 2018
Utility Installation	August 2018
Town Square	Summer 2019
Building top-out	August 2019
Building Close-in	October 2019
Interior build-out	Spring 2020
Substantial Completion	May 2020
Move-in (occupancy)	Summer 2020

Update your subscriptions, modify your password or email address, or stop subscriptions at any time on your [Subscriber Preferences Page](#). You will need to use your email address to log in. If you have questions or problems with the subscription service, please contact subscriberhelp.govdelivery.com.

This service is provided to you at no charge by [Department of Transportation](#) of [Montgomery County MD](#).

Visit [Wheaton Revitalization Project](#) page to learn more.
