




Fenton Village Bike & Pedestrian Projects

Project Newsletter #11, May 2024

Thank you for your interest in the Fenton Village bike and pedestrian projects! The Montgomery County Department of Transportation (MCDOT) is continuing planning efforts for the three related bike and pedestrian improvement projects in Fenton Village. We will provide regular updates through newsletters like this one.



project
webpage

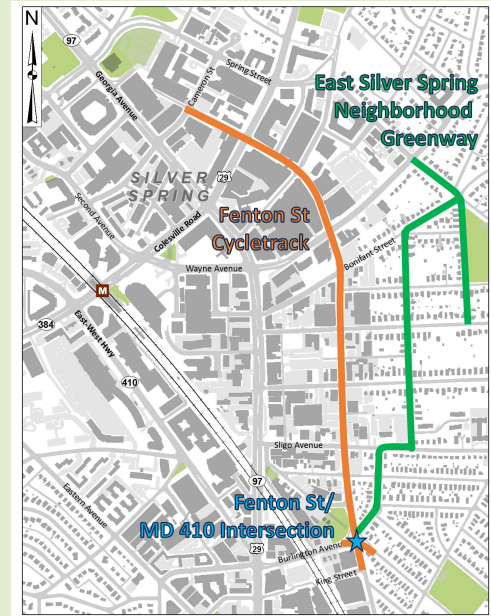

Fenton Street Cycletrack Update

Since the last project update in November 2022, we have been hard at work finalizing the design and working on both permitting and property acquisition. We recently completed the 100% design and are working on some minor tweaks due to utility changes. There have been no substantial changes to the design since the 65% stage. The plans and a video update from that stage are available on the project webpage, under the Project Documents tab.

Most of the work over the past year had focused on finalizing utility relocations. In addition to the power and telecommunication lines you can see on the poles along portions of Fenton Street, there are also a multitude of utilities hidden underground. Each of these needs to be a safe distance from other utilities. We have coordinated extensively with the utility companies and final utility design and approvals are currently underway. Some utility relocations may start this summer or fall.

We are also currently working to get permit approvals from several agencies, including the Montgomery County Department of Permitting Services, the Maryland State Highway Administration, and the Federal Highway Administration. We expect to receive all permits required for construction before the end of 2024.

Our property acquisition team is also working to acquire all necessary right-of-way or temporary construction easements. We expect this work to be completed by the end of 2024.

We expect to go to construction in early 2025. Construction is likely to take 18-24 months to complete. You may see some construction activity in advance of our work starting, as the utilities begin to relocate their facilities.

We will coordinate closely with businesses along the street, and will continue to post updates for residents. Please feel free to contact us with questions or concerns.

Updates At A Glance

This section provides a quick update of the status of each project.

Fenton Street Cycletrack

- Phase: Permitting & Property Acquisition
- Phase completion: Fall 2024
- Next phase: Utility Relocation
- Construction expected to start Spring 2025

Fenton St/MD 410 Intersection

- Now included with Fenton Cycletrack project

East Silver Spring Greenway

- Phase: 30% Design complete
- Next phase: Final Design
- Construction expected to start Spring/Summer 2025

Project Websites

<https://tinyurl.com/FentonVillage>
<https://tinyurl.com/Grove-Street>

PROJECT MANAGER

Matt Johnson

Phone: 240.777.7237

Matt.Johnson@MontgomeryCountyMD.gov

Division of Transportation Engineering

Phone: 240-777-7270

Twitter: @MCDOTnow



Web: <https://www.montgomerycountymd.gov/dot-dte/index.html>

For alternative formats of this newsletter, please contact us at 240-777-7623 (Voice). TTY users call Maryland Relay.

Fenton Street / MD 410 Intersection - Now a part of the Fenton Cycletrack Project

MCDOT originally anticipated that the Fenton Street / MD 410 Intersection Project could be constructed on a faster timeline than the rest of Fenton Street and made it a separate project for that reason. However, permitting delays have pushed the timeline back, and it now makes sense to construct this at the same time as the Fenton Street Cycletrack. From now on, the intersection project will be considered part of the larger Fenton Street Cycletrack project.

East Silver Spring Neighborhood Greenway Update

The East Silver Spring Neighborhood Greenway was designated by the Bicycle Master Plan, adopted in 2018. It starts at Cedar Street and Wayne Avenue and follows Cedar Street to Bonifant Street, then Bonifant Street to Grove Street, follows Grove Street to Sligo Avenue, then jogs along Sligo Avenue to Woodbury Drive, then runs down Woodbury Drive to Philadelphia Avenue. Based on concerns that the changes to Grove have pushed some traffic onto Houston Street, we are also including Houston Street in the scope of the project.

The map at right shows the scope of the East Silver Spring Neighborhood Greenway. Grove Street, which will get upgrades, is shown in blue. The other streets proposed for neighborhood greenway treatments are shown in green. The stretch of Sligo Avenue that will get a low-stress bike and pedestrian connection is shown in red. Houston Street is shown in yellow.

Along Grove Street and Houston Streets, the project will add sidewalks along the western sides of both streets. Grove will also have permanent traffic calming treatments added to replace the temporary pilot treatments that are currently in place.


Woodbury Avenue, Bonifant Street, and Cedar Street will also receive some traffic calming treatments. Along Cedar Street, the existing contra-flow bike lane will be moved so that it is against the western curb and parking will be flipped to be on the east side of the street. This will eliminate the current situation, where bicyclists are sandwiched between parking and traffic going in the opposite direction.

Along Sligo Avenue, a shared-use path will be constructed on the north side of the street between Woodbury Drive and Grove Street along with a signalized crossing for cyclists and pedestrians at Woodbury and Sligo.

We presented initial concepts to the community in the fall of 2023. Since that time, we have been working to refine the design based on feedback and have completed the 30% stage of design. We expect to go before the Montgomery County Planning Board in July or September 2024.

The next step following the Planning Board hearing will be to work on the final design. That process will take several months, and is expected to last through the end of 2024. As the project moves forward, we will need to work with the utility companies on potential relocations. We may also have some minor right-of-way acquisitions.

At this time, construction is unlikely to start before spring or summer 2025. Some elements may be constructed separately from others, so the project may not be built all at once.

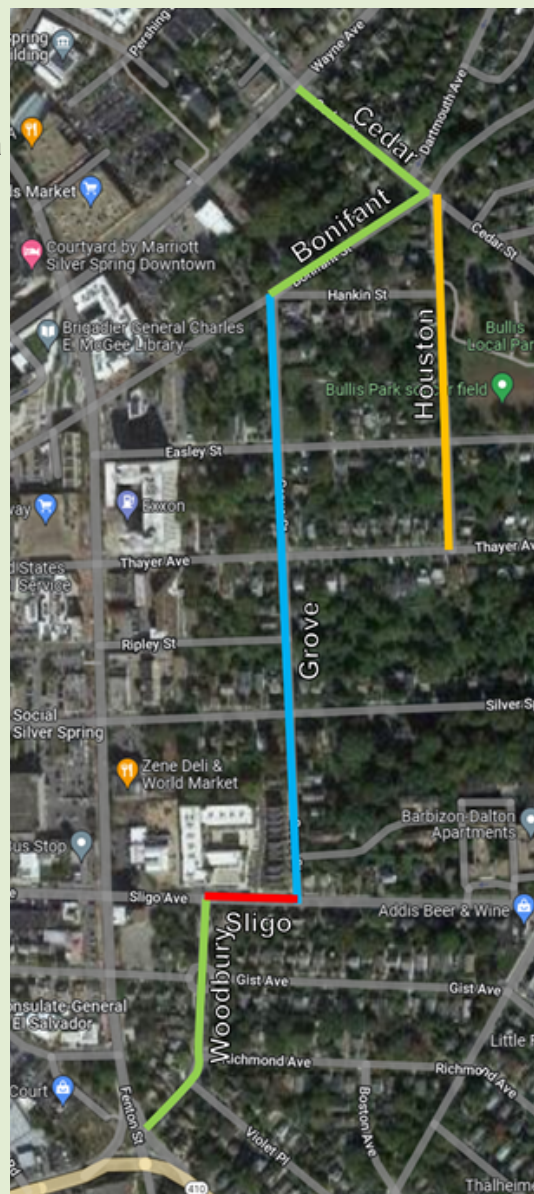

East Silver Spring Neighborhood Greenway map

To sign up for the project update mailing list, please send an email to Matt.Johnson@MontgomeryCountyMD.gov and indicate you're interested in the Fenton Village projects mailing list.

LOOK OUT
FOR EACH OTHER

Learn how to navigate new facilities:
www.montgomerycountymd.gov/lookout

VISION ZERO

NO TRAFFIC DEATHS BY 2030
