



## **Welcome to Wheaton Revitalization News!**

**Wheaton Revitalization News** is an email distribution list that will provide frequent updates to the surrounding community on the Wheaton Revitalization project. The purpose of this distribution list is to provide you with project updates and construction activities. For additional information on the Wheaton Revitalization Project please visit <http://www.wheatonproject.com>

### **Look Ahead - Week of August 12 to August 18, 2018**

#### **Executive Summary**

The project continues to track for an April, 2020 substantial completion.

#### **Headliner**

The contractor continues to progress with major concrete pours on garage Level P4 (lowermost level) and continues with elevated slab pours at Level P3 (see photo).

#### **Garage Construction**

Garage floors are numbered P4 (lowest level) through P0 (highest level)

#### **Level P4**

The contractor has one pour remaining to complete Level P4. As you may recall, Level P4 was designed to be constructed in ten pours. Pour ten is currently planned for Monday, August 13, weather permitting. When completed, this will conclude P4 construction and the building foundation.

#### **Level P3**


Construction of Level P3, the first elevated floor, is well underway (see photo). Level P3 will be constructed in six pours. The first pour was completed on August 7 and the second pour on August 10. The third pour is currently scheduled for Thursday, August 16.

#### **Building Walls**

Construction of the building walls will follow placement of the elevated slabs.

Numerous quality assurance/quality control (QA/QC) inspections continue daily to ensure that the concrete, waterproofing, and reinforcing systems have met specified QA/QC requirements. Rigorous inspections are conducted by third-party inspection firms, peer review experts, the contractor, and MCDOT, with oversight by the County's Department of Permitting Services (DPS). Quality is everyone's business!

***Pour No. 9  
Concrete Placement at P4***

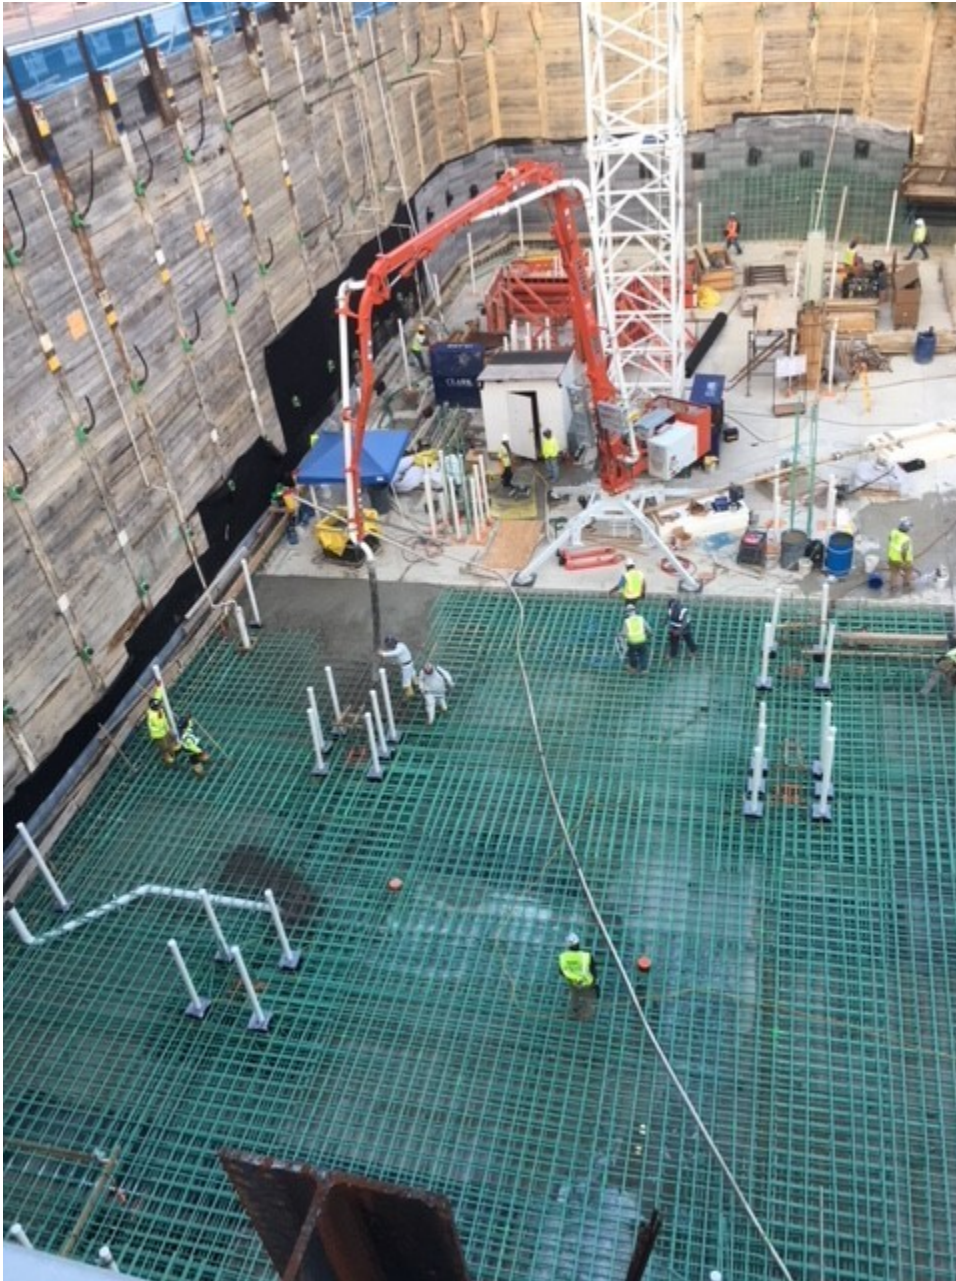


***Level P3 Elevated Slab  
Pour No. 1 (middle-foreground)***



*Level P3 under construction*



*Level P4  
Pour No. 10 (background)*

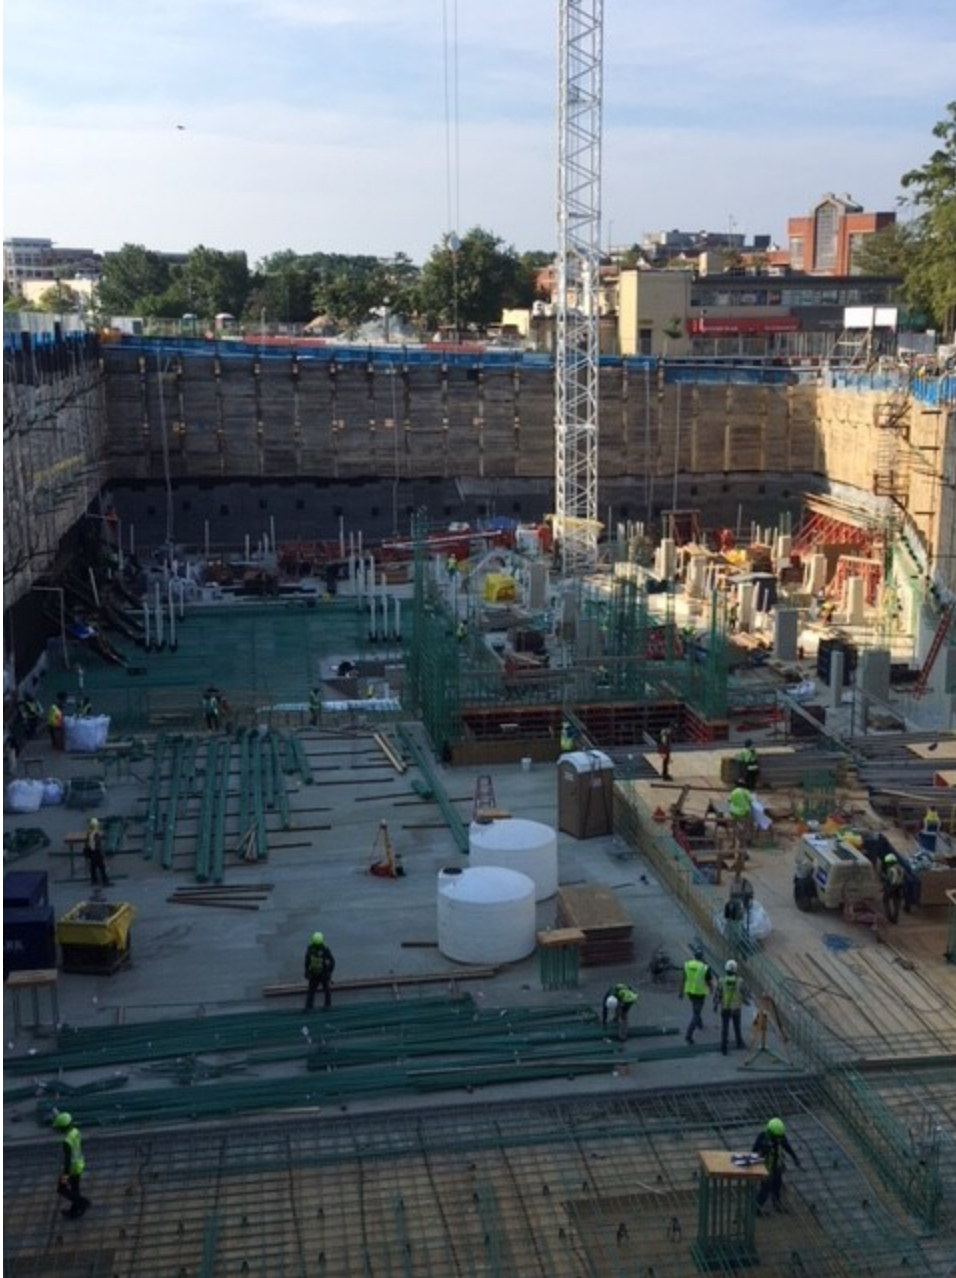

### **Utility Construction**

Utility construction continues along Grandview Avenue as Pepco is installing a medium-sized concrete vault beneath the sidewalk opposite the Washington Professional Systems (WPS).

Installing the underground vault is the last of the Pepco work along Grandview Avenue apart from a temporary pole to be installed in front of the Mayer Building. The pole will provide temporary power to the businesses to make way for removal of the overhead power lines along the east side of Grandview Avenue.

*Pedestrian traffic was temporarily detoured to the east side of Grandview Avenue*



### **Follow Project Progress via the Project Camera**

A camera has been installed to view construction on the site. [Click here](#) to access the camera.

### **Upcoming and Ongoing Activities**

- Concrete placement for garage Level P4 will be completed on August 13
- Garage Level P3 under construction (total of 6 pours)
- Placing waterproofing in advance of wall construction
- Wall pours
- Column pours
- Utility construction in Grandview Avenue

## Project Milestone Schedule

Activity	Completion Date
Demolition of RSC Bld.	Complete ✓
Building tie-down anchors	Complete ✓
Geothermal Piping	Complete ✓
Foundation Construction	Summer 2018
Building Reaches Street Level	December 2018
Utility Installation	Summer 2018
Town Square	Summer 2019
Building top-out	August 2019
Building Close-in	October 2019
Interior build-out	Spring 2020
Substantial Completion	May 2020
Move-in (occupancy)	Summer 2020

---

Update your subscriptions, modify your password or email address, or stop subscriptions at any time on your [Subscriber Preferences Page](#). You will need to use your email address to log in. If you have questions or problems with the subscription service, please contact [subscriberhelp.govdelivery.com](mailto:subscriberhelp.govdelivery.com).

This service is provided to you at no charge by [Department of Transportation](#) of [Montgomery County MD](#).

Visit [Wheaton Revitalization Project](#) page to learn more.
